

---

**MARCH 1, 2023**


# MRP Implementation Working Group: Market Participant Readiness Planning

# Purpose

- Provide an update to the IWG on Market Participant Readiness timelines, for discussion and feedback
- Insights will inform an update to the MP Readiness Plan

# Market Participant Readiness - Background

- The IESO has posted for stakeholder review a MP Readiness Plan and Day-In-The-Life summaries
- The Project Status has been updated with quarterly project financial information

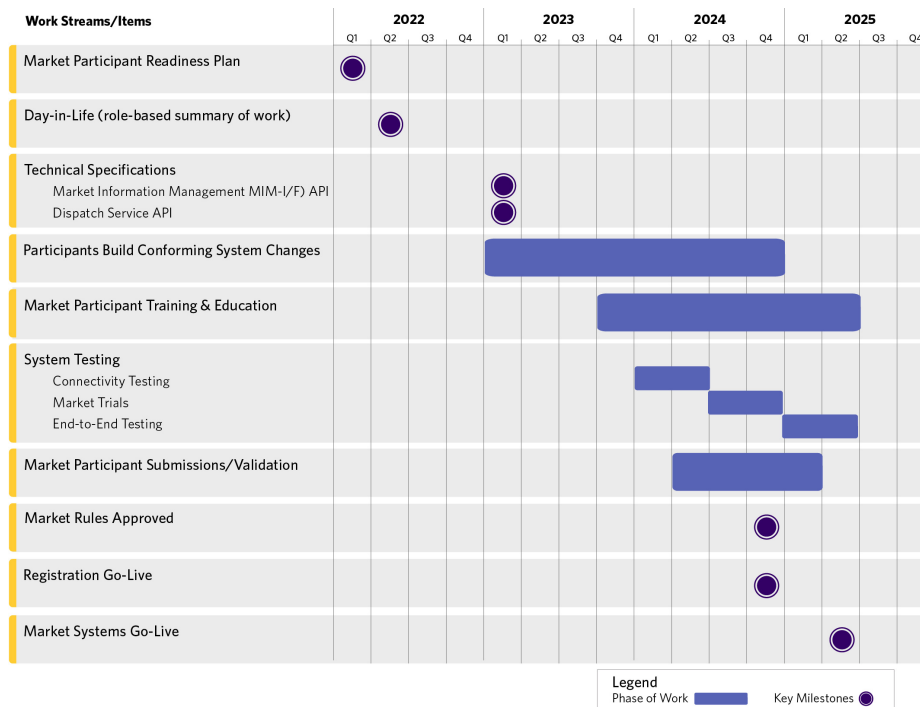

# Market Participant Readiness - Goals

- The IESO is planning to provide relevant information to enable participants to build a plan to resource the readiness activities for the renewed market
- Creates the commitment of where the IESO will provide support and training material
- The IESO will be surveying participants at various points throughout the process to measure MP activities to prepare for MRP
- Will lead to MP self-assessment for MRP readiness

# Market Participant Readiness Checklist

- The IESO is building a tailored checklist for market participants to highlight the required actions
- This will provide further detail to participants to begin to plan for resourcing Market Renewal training and testing activities
- Will be available by the end of March for stakeholder review

# MP Readiness Timelines


- March, 2023: Post API Technical Specs and MP Readiness Checklist
- June, 2023: Initial survey of MP Readiness
- October, 2023: IESO to post complete suite of training material, and begin direct outreach with participants
- December, 2023: Survey MP Readiness (beginning of quarterly surveys)

# MP Readiness Testing Timelines

- January, 2024: MPs to begin Connectivity Testing
- July, 2024: Market Trials for Online IESO, EMI and DS
  - Registration System live in late October, 2024
- January, 2025: End-to-End Testing Period
  - Defect resolution during unstructured testing until early March
- IESO to provide test plans and test cases in advance of each testing period

# MP Readiness Reports Timelines

- IESO Report sample and schema files will be published in 4 batches
- IESO will leverage the current Reports Sandbox to provide files

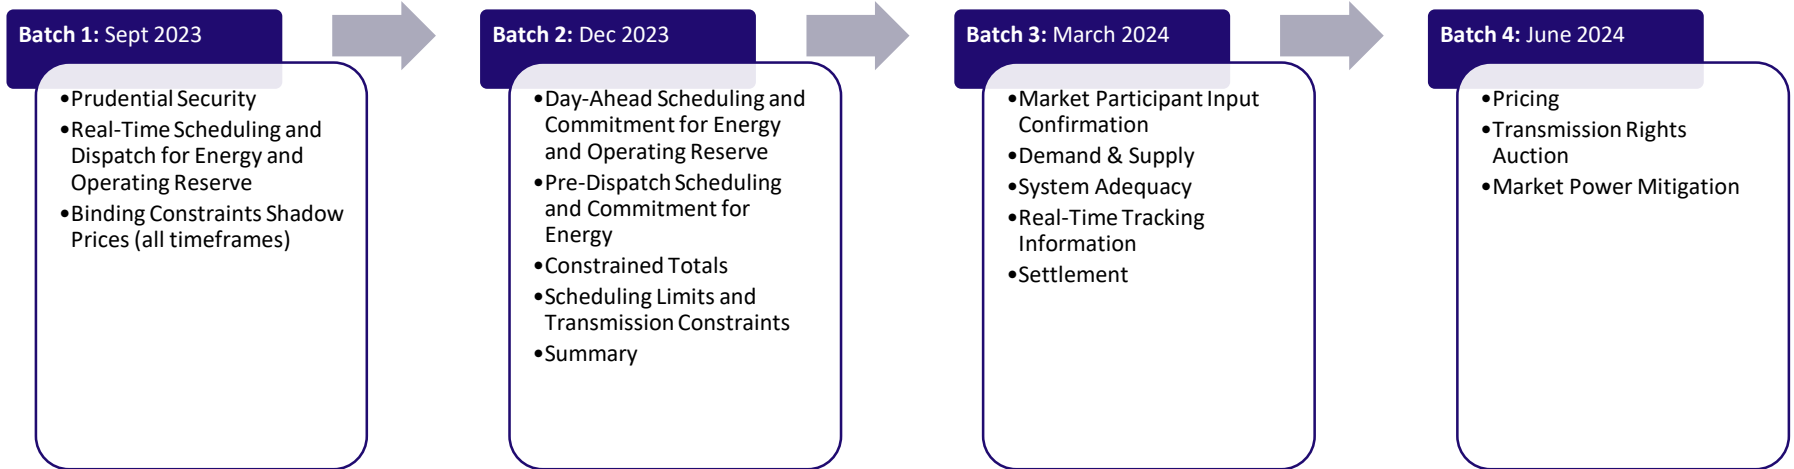



---

# Thank You

[ieso.ca](http://ieso.ca)

1.888.448.7777

[customer.relations@ieso.ca](mailto:customer.relations@ieso.ca)

[engagement@ieso.ca](mailto:engagement@ieso.ca)



[@IESO\\_Tweets](https://twitter.com/IESO_Tweets)



[facebook.com/OntarioIESO](https://facebook.com/OntarioIESO)



[linkedin.com/company/IESO](https://linkedin.com/company/IESO)
